

RISK ASSESSMENT & METHOD STATEMENT

Truss roof installation onto plots 98 to 112

(Flats/Apartments) 2

RE PLANT HIRE LTD © 2026
Company Established 1974



PURCELL AVENUE INDUSTRIAL ESTATE
PORT TALBOT
SOUTH WALES
SA12 7TZ

Method Statement

Risk Assessment No	4224
Customer/Site Address	Taylor Wimpy Bristol Stoke Rise Taylor Wimpey . Stoke Rise Curtis Lane , Stoke Gifford Bristol Avon BS34 8QG
Site Manager	Dan Budd 07823416633
Date of Lift	17 / 06 / 2026
Start Time on Site	8am
Plot Numbers	98 to 112
Truss Rack	NO
Road Plates	X 1
Lorry Loader	L114
Driver	Karl Peters
Banksman/Rigger Slinger	Nigel Doel

1. Scope of Works

Raising and positioning of roof trusses into their fixed positions onto roof level using HIAB digital control lorry c/w driver and rigger / slinger. Customer to prepare clear access at the location of lift. Transport of trusses on site if truss rack required. Haul road may need to be closed to do lift .

2. Management and Supervision

<i>Role</i>	<i>Name</i>	<i>CPCS/NPORS Card</i>	<i>HIAB Lorry Loader Certificate</i>	<i>Tackle Test Certificate</i>	<i>Rigger Slinger Card</i>
Operator	Karl Peters	✓	✓	✓	✓
Rigger Slinger	Nigel Doel	✓			✓
Appointed Person	Karl Peters	✓	✓	✓	✓

The Site Manager will supervise implementation of the approach/methodology and various risk control measures identified. Details as below:

Site Manager:	Dan Budd
----------------------	----------

3. Items to be Lifted/Weights of Materials

Type	Weight	To be Lifted
Roof Truss	500kg Approx	
Dormers	150-250kg Approx	
Spandrel Panels	250kg-500kg Approx	
Chimneys	250kg Approx	
Beams (wood) Beams (steel)	150-2000kg Approx	
Timber packs & Roof Ladders	300kg-1000kg	
Blocks / Bricks	1000-1500kg	✓

4. Related Documentation

This method statement is to be read in conjunction with the following documents

This method statement is to be read in conjunction with the following documents

- Lorry loader Safe Operator Procedure
- Beams and Roof trusses Risk Assessment

5. Acts, Regulations and Codes of Practice

All the below are codes and practices followed by the Company

- Health and safety at work act 1974
- Management of health and safety at work regulations 1999
- Provision & use of work equipment regulations 1998
- Manual handling regulations 1992
- Other: LEEA code of practice for the safe use of lifting equipment
- BS 7121 series: BS 7121-1:2016
- BS 7121-2-4 Inspection, maintenance and thorough examination – Loader cranes
- BS 7121-4 Code of practice for safe use of cranes – Lorry loaders
- HSE Guidance – Lifting Operations
- HSE GS6 Avoidance of danger from overhead power lines
- CPA Model Conditions for the Hiring of Cranes
- CPA Model Conditions for Contract Lifts.
- Health and Safety at Work etc. Act 1974
- Lifting Operations and Lifting Equipment Regulations 1998 (LOLER)
- Provision and Use of Work Equipment Regulations 1998 (PUWER)
- Construction (Design and Management) Regulations 2015 (CDM)
- Management of Health and Safety at Work Regulations 1999
- Workplace (Health, Safety and Welfare) Regulations 1992
- Work at Height Regulations 2005
- Personal Protective Equipment at Work Regulations 1992
- Reporting of Injuries, Diseases and Dangerous Occurrences Regulations 2013 (RIDDOR)
- Electricity at Work Regulations 1989
- LOLER Approved Code of Practice (L113).

6. Pre-Start Activities

- Position and direction of crane
- Direction of rotation
- Sotrage areas from where materials to be fitted
- Centre of radius
- Outrigger locations
- Max SWL at given radius
- Weight of loads to be ascertained
- Personnel competency checks to be completed
- Lifting equipment and accessory certification to be confirmed as current
- Ascertain from the foreman carpenter which side guide ropes are to be attached.

7. Approach/Methodology

After completion of all the above pre-start activities, work will commence following the procedure below. If at any point something changes which requires amendments to the following procedure, work must be stopped and the safe system of work reviewed and methodology rewritten. Under no circumstances must work be carried on outside of this procedure.

Control Measures

- Upon arrival and prior to commencing work activity, personnel to report to Site Manager to sign in and attend site induction. HIAB lorry to be parked in designated area and site speed restrictions abided by at all times.
- The lift area will cordon off to prevent access for unauthorised personnel.
- Customer to prepare, clear access to the front of the house using hardcore to level and compact the area where the HIAB will be located to process task of truss lifting.
- The Appointed Person has the responsibility to assess the site and if they feel it is unsafe to proceed they will stop the work and discuss their concerns with a Site Manager; i.e. overhead power cables and unsuitable ground conditions.
- Should any reversing be involved with this procedure the banksman will aid the lorry loader operator, particularly when the reversing procedure involve confined/blind movements.
- The appointed person will draw up a plan of the work area when the site visit is carried out - this is agreed with the HIAB operator and Site Manager before work commences.
- The lorry loader operator will then set-up the lorry loader as per the manufacturer's instructions. The outriggers pads must be a minimum of 400mm. SWL of lorry loader and tackle must not be exceeded; Angle of chains and slings should not exceed 45° and truss hook not overloaded.
- The lorry loader operator will raise crane and position over the centre of the item/s to be lifted.
- When crane operation complete, the lorry loader operator will remove lifting tackle from crane hook, stow crane and lifting equipment in travel position and make all senior site personnel that lifting operations have finished
- Appointed first aider and provision of fire equipment should stated at site induction
- Emergency Contact for RE Plant Hire Ltd is James Tandy (Depot Manager); [01639 886966](tel:01639886966)
- Crane outrigger legs to be fully extended over the side where lifting is to be carried out
- If remote battery needs to be changed, HIAB Operator should not drop or throw battery from the scaffolding, batteries should be passed from hand to hand.

Method Statement – Loading / Unloading / Transporting Trusses with Truss Rack

Site Manager to prepare suitable area adjacent to truss storage compound for HIAB crane to be set up.

- Position ladder on firm level ground to the top of the roof truss pack, footed by either senior site personnel or ladder foot.
- Slew HIAB over top on roof trusses and position endless sling around apex of roof truss pack (not in choke).
- Banksman to descend ladder and place in safe area prior to lift process
- Operate HIAB crane to lift roof truss pack onto truss rack deck, where applicable use rope and ratchet straps as a restraint.
- After materials have been safely restrained, lower HIAB and ascend ladder footed at all times to retrieve lifting slings from apex of roof truss pack
- Secure ladder on ladder rack / storage area and lifting equipment in storage boxes.
- Stow crane into travel position prior to transport to lift zone
- Once at lift area / plot, trusses must be lifted off the truss carrier / rack onto ground level adjacent to either the scaffolding or lorry.

Method Statement – Lifting and Slings Roof Trusses

- Depending on the volume of trusses needed at any one time either the truss hook or a 3 tonne endless sling can be used.
- If a pack of more than seven have to be lifted then use a 3 tonne endless sling, be mindful of sharp edges towards the apex of the roof truss where the two sides are joined.
- When using an endless sling to lift more than seven trusses, the sling should never be slung over the truss hook, only the main / fly-jib hook. This will prevent the truss hook being overloaded and point loaded.
- When lifting seven or under at anyone time, attach truss hook attachment to fly-jib.
- If the trusses are flat against each other, the pack must be split to allow room for truss hook to be attached. If banksman is unable to do this on his own, Appointed Person / foreman carpenter must assist.
- Once the hook has been attached to the apex of the roof trusses guide rope to one side must be attached. (Side ascertained at site induction / sign in)
- Banksman to stand appropriate distance away from trusses, grip guide rope and acknowledge to crane operator that trusses may be raised by means of appropriate hand signals.
- Trusses to be positioned as per instructions from foreman carpenter.
- Ensure that crane remote is locked off whilst trusses are being fixed.
- Only remove truss hook from truss on confirmation from foreman carpenter.
- Once fixed into position, guide rope to be handed back to banksman and process is repeated.

Method Statement – Lifting and Slings Spandel Panels

- Attach truss hook to main / fly-jib hook
- NB in the majority of cases the lifting slings fitted to the panels are single lift only
- Sling under two number duplex sling lifting points and position endless sling at each end of truss hook
- Be sure to have the correct length so that the spandrel panel lifts correctly and not to one side
- Attach guide rope by bending nail around carabineer with hammer.
- Banksman to stand appropriate distance from spandel panel and notify operator to lift item by appropriate hand signals.
- Panel is lifted and positioned into place under the instructions of the foreman carpenter.
- Operator to remove slings from fixed duplex webbing straps of spandel panel.
- Spandel Panels to be positioned as per instructions from foreman carpenter.
- Ensure that crane remote is locked off whilst Spandels are being fixed.
- Only remove truss hook from truss on confirmation from foreman carpenter.

Method Statement – Lifting and Slings Chimneys

- Make sure all lifting eyes are screwed into chimney (finger tight).
- Attach small 4.25 tonne chains to main hook of fly-jib.
- Attach chain hooks to lifting eyes, also attach tag rope to lifting eye.
- Banksman to stand appropriate distance from chimney before giving signal to operator that item can be lifted.

- Chimneys to be positioned as per instructions from foreman carpenter.
- Ensure that crane remote is locked off whilst chimneys are being fixed.
- Only remove truss hook from truss on confirmation from foreman carpenter.

Method Statement – Lifting and Slings Packs of Timber & Roof Ladder trusses

- Only use the truss hook for lifting timber packs, if pack weight does not exceed 600kg. Otherwise you must use the main crane hook / fly-jib hook only.
- AT all times use two three tonne endless slings to lift ladder trusses as this will allow correct rigging angle
- USE TAG LINE AT ALL TIMES

•

Method Statement – Lifting and Slings Wooden and Steel Beams

- It is unlikely that laminate beams or steel RSJ beams will exceed 2000kg in weight. Therefore the use of two 3 tonne endless slings shall be used for lifting the above items
- Ensure that items to be lifted are rigged to allow them to be as near to level as possible (choke position).
- Always be aware of hook turning when weight is taken, as load will find its centre.
- DO NOT use truss hook for lifting the above under any circumstances.
- USE TAG LINE AT ALL TIMES

Method Statement – Lifting and Slings Dormers

- Pre cast dormer units will vary in weight and dimension.
- Ascertain optimum lifting point when slinging to allow dormer to hang as near as possible to the vertical
- Be aware of fragile e.g. fiberglass content within the construction of dormers
- Inspect prior to lift and report any existing damage
- USE TAG LINE AT ALL TIMES

• Method Statement – Crane / Pallet forks

- See supplementary procedure on crane fork operation and safe working procedure

• Emergency Procedures

- In the event of an accident happening, notify Site Manager or senior site personnel immediately along with James Tandy without delay. Also notify Hire Desk. ([01639 886966](tel:01639 886966))

- Wind Conditions;

- Crane manufacturer states that the max wind speed is 50Km/h , please refer to Beaufort scale and extract from manual in Appendix. As different items react in different ways in the wind, this max value may be reduced depending on the height and radius of lift. Driver / operator to refer to Beaufort scale and if in doubt use hand held anemometer to confirm wind speed if intensity based on observed conditions are poor or worsen. If the Operator / Appointed Person is in any doubt that all or some items are not safe to lift they can liaise with Site Management and Carpenters to either wait until conditions improve or call the lift off.

On Completion of Installation

- Gather attachments and lifting tackle together
- Position outrigger legs and pads into travel position.

Sign out and make your departure known to senior site personnel.

Please note: CPA Contract Lift terms and conditions apply

8. Lifting/Accessory Details

<i>Accessory</i>	<i>Required</i>	<i>SWL</i>
4 leg chain set	YES	4.25 & 6.6ton
Truss Hook	YES	600kg
Road Plates	YES	N/A
Nylon Endless Slings	YES	3000kg
Truss Rack	YES	N/A
Bow Shackles		3 TON
Crane forks / Pallet		2000kg
Brick Grab and net		1000kg

9. Personal Protective Equipment

In accordance with Company site rules, personnel must wear hard hats, safety boots and high visibility jackets/vests and gloves at all times in work areas. The work covered by this method also requires:

<i>Item</i>	<i>Required</i>	<i>Item</i>	<i>Required</i>
Hard Hat and Chin Strap	✓	Safety Footwear	✓
Hi visibility jacket / vest (yellow or orange)	✓	Ear Muffs or Ear Plugs	✓
Waterproofs	✓	Fall arrest block 12-15m	✓
Gloves	✓	Light Eye Protection or Hi-Impact Goggles	✓

10. Emergency Procedure/Rescue Plan

Details in the event of an emergency

Appointed First Aider	As per site Induction
Location of First Aid Equipment	As per Site Induction
Provision & Location of Fire Equipment	Site office or as per induction
All Accidents/Incidents to be Reported to	Senior Site Manager
Site-Specific Safety Instructions	As per site induction
Contact Person/Health & Safety Manager	RE Plant Hire Ltd Depot (01639 886966) and James Tandy Director (option2)

11. Lift Plan

Position of HIAB for lift

BLANK

NOTE:
Lifting plan to include –
Site Name, Plot Number,
Location of HIAB in
relation to the work task

Check scaffold safety tag
prior to accessing

Position of safety signs
and cones / bunting
(marked by X around HIAB
in drawing)

Position of HIAB vehicle
may change on day of lift
due to unforeseen
circumstances
Refer to HIAB chart on
separate page for SWL at
the above radius

Notes

Continued

For Office Use Only

RE PLANT HIRE LTD.
Going that extra distance

Name	Signed	Date	
Drawn by	Checked by	Approved by	Date
Block No.			Revision





12. Site Plan



13. Lorry Loader/Crane Details

Name	L114
Status	Active
Crane Type	Palfinger PK65002
Capacity	13,400 KG
Max Jib Length	30 metres
Max Radius	30 metres
SWL at Max Radius	700kg
Outrigger Type	Up to Full depending on site conditions
Outrigger Max Ground Pressure (without pad)	20,000 daN
Weight of Hook Block	N/A
Fly-Jib	PJ125-FLY-JIB

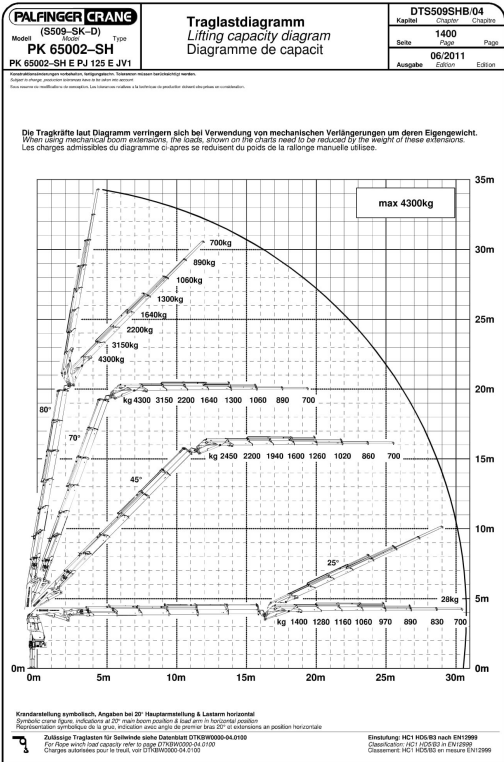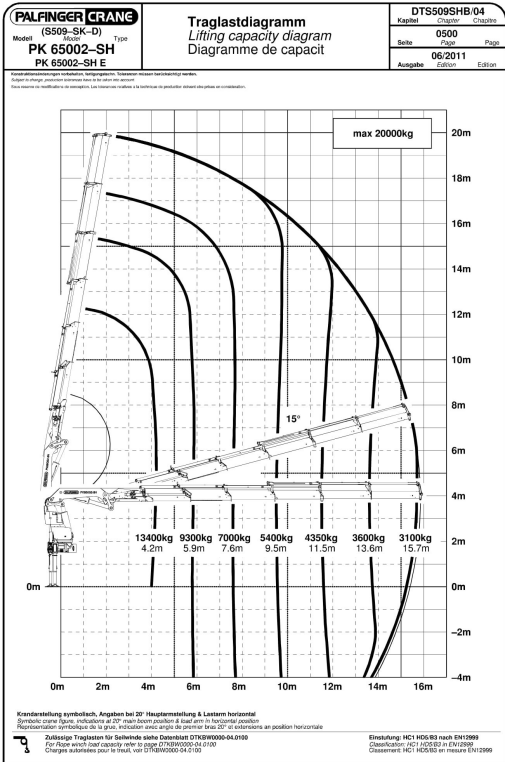

14. Briefing

The work activity briefing is intended to be a two-way process and all operatives are expected to challenge the proposed approach, particularly if they feel that a safer and more practical work method can be adopted. All personnel will sign the printed document to confirm that they understand the content of this risk assessment.

Time of toolbox talk given: (Below to be confirmed on day of lift)

<i>Position</i>	<i>Name</i>	<i>Signature</i>	<i>Company</i>	<i>Date</i>
HIAB Operator	Karl Peters		RE Plant Hire Ltd	
Foreman Carpenter				
RIGGER / BANKSMAN	Nigel Doel		RE Plant Hire Ltd	
Lift Supervisor	Karl Peters		RE Plant Hire Ltd	
Driver	Karl Peters		RE Plant Hire Ltd	
Banksman/Rigger Slinger	Nigel Doel		RE Plant Hire Ltd	
Site Manager	Dan Budd		Taylor Wimpy Bristol	

15. Appendices

Chapter 2 — General specifications

(FASSI)

Service and storage conditions



The non-conformity with service conditions may cause both hazards for operator and persons in the vicinity and damages to crane and things.

The crane is designed to be used in the temperature range indicated in the following table. If the temperature range for crane operation is not included in these limits, the crane functionality may be discontinuous and damages to the hydraulic and electrical systems may occur.

Temperature range for operation and storage of the crane	
Temperature of the crane working environment	-30°C to +50°C
Temperature of the crane storage environment	-40°C to +70°C



In case of work in another temperature range than the one prescribed in the table, it is compulsory to request FASSI specific authorization.

The crane must be used with wind speed lower than 13,8 m/s (50 Km/h - maximum value of degree 6 of Beaufort scale) and in absence of thunderstorms.


Force of the wind (Beaufort scale)	Wind speed (m/s)	Classification	Characteristics
0	0,0 ÷ 0,2	Calm	Calm wind, smoke goes up quite vertically.
1	0,3 ÷ 1,5	Light breeze	Smoke reveals the direction of the wind, one can feel the wind blowing, leaves start fluttering.
2	1,6 ÷ 3,3		
3	3,4 ÷ 5,4	Moderate breeze	Leaves and branches are in constant motion, small branches start fluttering. Dust and papers dance on the ground.
4	5,5 ÷ 7,9		
5	8,0 ÷ 10,7	Fresh breeze	Small green branches bend, the surface of waterways and lakes is wavy.
6	10,8 ÷ 13,8	Near gale	Big branches bend, wind whistles through high-tension cables, it's difficult to walk keeping the umbrella open.
7	13,9 ÷ 17,1	Moderate gale	Trees sway, it's hard to walk.
8	17,2 ÷ 20,7	Storm wind	Branches get broken, it's hard to walk.
9	20,8 ÷ 24,4	Storm	It damages houses (antennas and roof tiles fall down).



While working with the crane vertical up, it is recommended to consider the working limit speed of the wind decreased of 5 km/h every 10 m height (refer to EN 1991-1-4).




Procedure: Rigging Method Statement RE 01

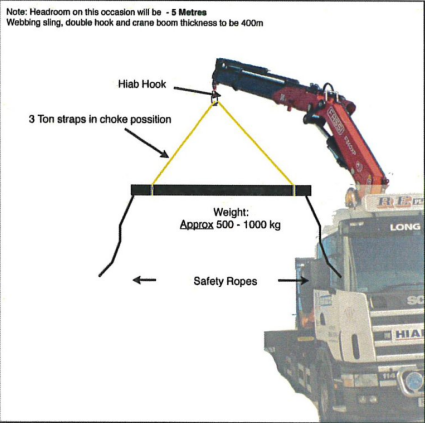


Note 1 no polyester duplex webbing sling in choke position 3 ton x .8 = 2.4 ton SWL

Procedure: Rigging Method Statement -

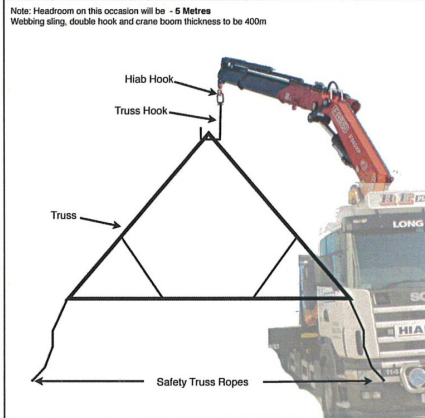


Note 1 no polyester duplex webbing sling in choke position 3 ton x .8 = 2.4 ton SWL
Note 1 no truss hook SWL 650kg

Procedure: Rigging Method Statement RE 01

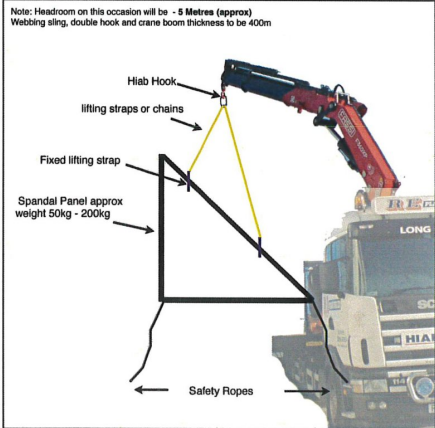

Note 2 no polyester duplex webbing sling, 3 ton SWL

Procedure: Rigging Method Statement RE 01

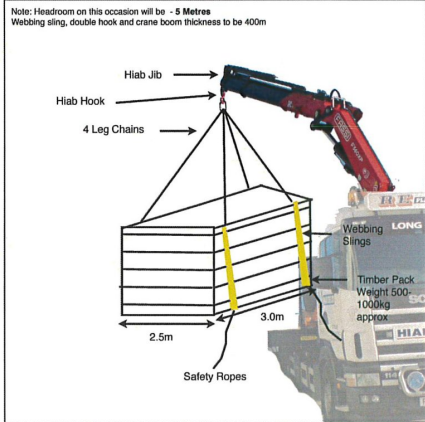

Note 1 no polyester duplex webbing sling in choke position 3 ton x .8 = 2.4 ton SWL
Note 1 no truss hook SWL 650kg
4 Leg Chains 6.5 Ton

Risk Assessment

Risk Matrix (Guide)					
SEVERITY \ PROBABILITY	Improbable	Remote	Possible	Probable	Likely
Fatality	MEDIUM	HIGH	HIGH	VERY HIGH	VERY HIGH
Major Injury	MEDIUM	MEDIUM	HIGH	HIGH	VERY HIGH
Reportable Injury	LOW	MEDIUM	MEDIUM	HIGH	HIGH
Lost Time Injury	LOW	LOW	MEDIUM	HIGH	HIGH
Minor Injury	LOW	LOW	LOW	MEDIUM	HIGH

<i>Hazard</i>	<i>Person(s) at Risk</i>	<i>Risk Level</i>	<i>Control Measures</i>	<i>Residual Risk</i>
Overloading of lorry loader crane	Crane operator, Site Operatives, lift supervisor	High	- Crane lifting capacity to be identified on the crane and duty charts available in the cab. - Weights of loads to be established. - SWL of the lorry loader crane will not be exceeded. - Ground conditions to be confirmed. - Radius of lift to be ascertained for load. - Operator competency checks. - Slinger/banksman competency checks. - Operator/User instructions and duty charts shall be available in cab. - Current certificate of thorough examination / inspection shall be available in the cab.	Low
Overloading of lifting accessories.	Crane operator, Site Operatives, lift supervisor	Medium	- Lifting accessories SWL requirements to be confirmed. - SWL of the lifting accessories will not be exceeded. - Lifting accessories to be attached and used as intended. - Pre-use inspections to be undertaken to check for damage. - Non-standard or modified lifting accessories shall not be used. - Operator/User instructions shall be briefed to those involved in the lifting operation. - Operators shall be trained and competent in the use of the lifting accessories provided. Training records available. - Current certificate of thorough examination / inspection shall be available in the cab.	Low
Slip/drop load	Crane operator, Site Operatives, lift supervisor	Medium	- Competent experienced HIAB Operator to be used for all lifting operations. Training records available. - Manufacturer or supplier recommended lifting points to be used at all times. - DO not overload truss hook - When lifting packs of wood and beams, evenly spread slings to the centre of the lift.	Low
Collision with obstructions	Crane operator, Site Operatives, lift supervisor	Medium	- Allow when planning for adequate clearances to avoid conflict with other plant or adjacent structures and to prevent over sail. - Use tag lines to help control the load.	Low
Over-Slewing	Crane operator, Site Operatives, lift supervisor	High	- Competent experienced HIAB Operator to be used for all lifting operations. Training records available. - HIAB Operator, Slinger/banksman shall ensure that all personnel are clear of loads prior to lifting. - Only those essential to the lifting operation shall be present and at no time shall the load be above workers.	Low

Overturning lorry loader/ crane.	Crane operator, Site Operatives, lift supervisor	High	• Crane lifting capacity to be established. • Weights of loads to be established. • Ground conditions to be confirmed by site. Underground services to be made known in site induction (and site visit) to HIAB Operator (Appointed Person) and appropriate signage on site, Excavations to be barriered off by Customer. Soft ground conditions to be made aware to the HIAB Operator at point of site induction. • Radius of lift to be ascertained for load. • HIAB Operator competency checks. • Slinger/banksman competency checks. • Refer to load chart for lifting capacity of crane. • Access and egress to lifting area is suitable for equipment being used, • Areas of soft ground shall be avoided.	Medium
Weather conditions.	Crane operator, Site Operatives, lift supervisor, Electrician, Engineers, Carpenters.	Medium	• Lifting operations will cease when ground conditions deteriorate following heavy rain, snow, ice etc. • Driver to confirm whether wind conditions are safe to carry out lift. • Lifting operations to cease during thunder storms.	Low
Working at height.	Crane operator, banksman	High	• Work from ladders is of short duration and three points of contact to be maintained. Ladder secured or footed. • RE Plant Hire personnel to have current training for working at height. • Site Manager to supply banksman to RE Plant Hire when required. • Scaffolding to be certified and tagged by competent persons before use. • Soft landing bags or birdhouse to be in place before work commences. • Never lean over scaffolding.	Medium
Working off ladder.	Crane operator, banksman	High	• Ladder to be footed or secured at top at all times. • Correct length for the requirement. • Ladder to be inspected before each use. • Work is of short duration and therefore is permitted. • Periodic inspections of ladders undertaken and documented records available.	Low
Overhead services.	Crane operator, banksman	High	• No lifting to be undertaken under overhead cables. • Site supervisor to set up demarcation barrier as required in line with GS6 and advice from service owner.	Medium
Manual handling.	Crane operator, banksman	Medium	• Sufficient operatives for tasks. • All staff to be trained in manual handling techniques. • 2 person lift or split load to be considered for heavy lifts.	Low
Slips, trips and falls.	HIAB Operator, banksman & Site Operatives	Medium	• Customer to make sure cables to be routed in prescribes zones. • Customer to make sure all waste materials to be removed from site. • Care to be taken around uneven ground on site	Low
Electric shock.	HIAB Operator, banksman & Site Operatives	Medium	• No working near power lines	Low
Contact with moving vehicles on site.	HIAB Operator, banksman, Site Operatives	High	• Care to be taken around vehicle access routes. • Pedestrian walkways to be used where available. • Speed limits, one way system and traffic calming to be adhered to where in use. • Hi-visibility clothing to be worn. • Care taken around heavy plant and machinery.	Medium
Contact with Effluent materials and contaminants	HIAB Operator, banksman, Site Operatives	Medium	• Food and drink to be consumed in designated area. • Wash facilities to be provided by client. • Avoid contact with unknown substances. • Report any spillages to site management immediately. • Antibacterial wipes available for HIAB operator and banksman in cab (If in low volume, let management know immediately)	Low

Falling objects	HIAB Operator, banksman, Site Operatives	Medium	• Wear appropriate PPE at all times. • Site signage visible where applicable. • Controlled access to work areas.	Low
Open excavations	HIAB Operator, banksman, Site Operatives	High	• Customer to ensure that all open excavations are barriered off • Appropriate signage visible to all site operatives • Dangers highlighted at site induction	Medium
Excess building materials around lift zone	HIAB Operator, banksman, Site Operatives	Medium	• Customer to clear and prepare access to where HIAB is to carry out roof truss install	Low
Working on truss rack	HIAB Operator, banksman,	Medium	• Once trusses and materials transported to lift point, unload trusses to ground level before commencing work N/A	Low
Other Lifting operations	HIAB Operator, banksman, Site Operatives	Medium	• Site Manager to make site operatives aware of any other lifting operations being carried out on site • Each lift to be cordoned off and only accessed by trained and competent operatives.	Not set
Pallet fork operation	HIAB Operator, banksman, Site Operatives	Medium	• Operatives should read and understand operating prcedure of pallet forks prior to commencing lift • SWL should never be exceeded • Brick net supplied should be used in accordance with the safe working procedure	Low

<i>Revised by:</i>	Ashley Leahy Appointed Person NPORS 496667		
<i>Assessed by:</i>	James Tandy - Appointed Person NPORS 353983 Mike Tandy - Appointed Person NPORS 332566		
<i>Actioned by:</i>	Dan Budd		
